

									9%					
ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	September	October	November	December	January	February		
1	<b>Power School Project Impmentation</b>	226 days	Mon 10/20/08	Mon 8/31/09										
2	<b>Project Planning / Management</b>	2.5 days	Tue 10/28/08	Thu 10/30/08										
3	Plan the Project (kickoff call)	0.5 days	Tue 10/28/08	Tue 10/28/08		PowerSchool,District								
4	Identify Technical Contacts	0.5 days	Wed 10/29/08	Wed 10/29/08		District								
5	Identity Initial Hardware and Systems Requirements for Project Phase 1	0.5 days	Thu 10/30/08	Thu 10/30/08		PowerSchool,District								
6	<b>District Change Management Overview</b>	28 days	Wed 10/8/08	Fri 11/14/08										
7	Software Preview with Tech Committee	0.5 days	Wed 10/8/08	Wed 10/8/08		PowerSchool,District								
8	Conduct Feasibility Analysis	0.5 days	Fri 10/31/08	Fri 10/31/08	5	PowerSchool,District								
9	Identify Training Needs for Org. Groups	1 day	Fri 11/14/08	Fri 11/14/08	8	PowerSchool,District								
10	<b>Booking Training and Implementation</b>	4 days	Tue 11/18/08	Fri 11/21/08										
11	Secure Resources for Training	0.25 days	Thu 11/20/08	Thu 11/20/08	13	District								
12	Schedule Initial Product Training	1 day	Tue 11/18/08	Tue 11/18/08	3	PowerSchool,District								
13	Review Scheduling needs	1 day	Wed 11/19/08	Wed 11/19/08	12,3	PowerSchool,District								
14	Schedule - Prepare to build training - direct with training	0.5 days	Thu 11/20/08	Thu 11/20/08	13	PowerSchool,District								
15	Schedule - Build Workshop - direct with training	0.5 days	Thu 11/20/08	Thu 11/20/08	13	PowerSchool,District								
16	Schedule Load training	1 day	Fri 11/21/08	Fri 11/21/08	13	PowerSchool,District								
17	<b>Purchase and Prepare Hardware</b>	18 days	Mon 11/10/08	Wed 12/3/08										
18	Hardware Purchase	10 days	Mon 11/10/08	Fri 11/21/08	3	District								
19	Hardware Preparation	3 days	Mon 12/1/08	Wed 12/3/08	18	District								
20	<b>Prepare for PowerSchool Installation</b>	4.25 days	Thu 12/4/08	Wed 12/10/08										
21	Configure Server and Install Timbuktu	1 day	Thu 12/4/08	Thu 12/4/08	19	District								
22	Submit Install Request Form	0.25 days	Fri 12/5/08	Fri 12/5/08	21	PowerSchool,District								
23	Install PowerSchool	3 days	Fri 12/5/08	Wed 12/10/08	22	PowerSchool								
24	<b>Business Review</b>	2 days	Thu 12/4/08	Fri 12/5/08										
25	Gather Data for District Setup - Form A	1 day	Thu 12/4/08	Thu 12/4/08		District								
26	Gather Data for School Setup - Form B	2 days	Thu 12/4/08	Fri 12/5/08		District								
27	<b>Logging onto PowerSchool</b>	1 day	Wed 12/10/08	Thu 12/11/08										
28	Create Implementation Team User Logins	1 day	Wed 12/10/08	Thu 12/11/08	23	District								
29	<b>System Settings</b>	1 day	Thu 12/11/08	Fri 12/12/08										
30	Set System Settings	1 day	Thu 12/11/08	Fri 12/12/08	28	District								
31	<b>District Setup</b>	1 day	Mon 12/15/08	Mon 12/15/08										
32	Set District Settings	1 day	Mon 12/15/08	Mon 12/15/08	25,28	District,PowerSchool								
33	<b>School Setup</b>	2 days	Tue 12/16/08	Wed 12/17/08										
34	Set School Settings High School/Middle School for 2008/9	2 days	Tue 12/16/08	Wed 12/17/08	25,28	District,PowerSchool								
35	Set School Settings for Elementry Schools for 2008/9	1 day	Wed 12/17/08	Wed 12/17/08										
36	<b>Importing Data - Phase I Scheduling</b>	19 days	Wed 12/17/08	Mon 1/12/09										
37	Extract Basic Data from Legacy System	5 days	Wed 12/17/08	Tue 12/23/08		District,PowerSchool								
38	Convert Data into Templates - PowerSchool_templates.xls	5 days	Wed 12/17/08	Tue 12/23/08		PowerSchool								
39	<b>Review and Import Data 'Core Data'</b>	5 days	Tue 1/6/09	Mon 1/12/09		District,PowerSchool								
40	Basic Students, Staff, Courses 2008/2009 data	3 days	Tue 1/6/09	Thu 1/8/09	32,34,3	District,PowerSchool								
41	Sections, Section Enrollment 2008/2009 data	2 days	Fri 1/9/09	Mon 1/12/09	40	District,PowerSchool								
42	<b>Importing Data - Phase II - All Non-Scheduling Data Starting June</b>	7 days	Wed 7/1/09	Thu 7/9/09										
43	Historical Grades, (2nd Pass Prior to go live)	2 days	Wed 7/1/09	Thu 7/2/09	40	District,PowerSchool								
44	Standards for elementary report cards	2 days	Thu 7/2/09	Fri 7/3/09		District,PowerSchool								
45	State Reporting Info/Additional Student Info Immunizations/Parent Contact/Lunch/Custom Fields	5 days	Fri 7/3/09	Thu 7/9/09	43	District,PowerSchool								



Project: PowerSchool Project Impleme  
Date: Fri 3/6/09

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

9%							September	October	November	December	January	February
ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names						
46	<b>Data Validation - Phase I Scheduling Data</b>	1 day	Fri 1/16/09	Fri 1/16/09								
47	Validate Data Accuracy	1 day	Fri 1/16/09	Fri 1/16/09	32,34,31	District,PowerSchool						
48	Review Setup	1 day	Fri 1/16/09	Fri 1/16/09	32,34,31	District,PowerSchool						
49	<b>Data Validation - Phase II Scheduling Data</b>	2 days	Tue 7/14/09	Wed 7/15/09								
50	Validate Data Accuracy	1 day	Tue 7/14/09	Tue 7/14/09	32,34,31							
51	Review Setup	1 day	Wed 7/15/09	Wed 7/15/09	50,32,31							
52	<b>Setting User Security</b>	147 days	Fri 12/19/08	Mon 7/13/09								
53	Setup Security Groups for Administrators	2 days	Fri 12/19/08	Mon 12/22/08	28	District						
54	Setup Page Access Permissions for Administrators	2 days	Tue 12/23/08	Wed 12/24/08	53	District						
55	Setup Teacher Groups and Access Permissions	1 day	Mon 7/13/09	Mon 7/13/09	28	District						
56	<b>Training Preparation</b>	75 days	Thu 1/29/09	Wed 5/13/09								
57	PowerScheduler Preparation	1 day	Thu 1/29/09	Thu 1/29/09	41	PowerSchool,District						
58	PowerTeacher Preparation	1 day	Fri 5/8/09	Fri 5/8/09	41,57	District						
59	Establish PowerTeacher -related Policies and Procedures	1 day	Mon 5/11/09	Mon 5/11/09	58	District						
60	Distribute PowerTeacher Documentation	2 days	Tue 5/12/09	Wed 5/13/09	59,54	District						
61	<b>Initial Product Training - Phase I for System Administrators and School Schedulers</b>	4 days	Mon 2/2/09	Thu 2/5/09		District,PowerSchool						
62	System Administrator and Intro to PowerSchool	1 day	Mon 2/2/09	Mon 2/2/09		District,PowerSchool						
63	Attend Prepare to Load Class	1 day	Tue 2/3/09	Tue 2/3/09	62	District,PowerSchool						
64	Working with Groups of Students	1 day	Wed 2/4/09	Wed 2/4/09	63	District,PowerSchool						
65	Attend Prepare for Load Class	1 day	Thu 2/5/09	Thu 2/5/09	64	District						
66	<b>Scheduling Project Management for 2009-10 School Year</b>	77 days	Mon 2/23/09	Tue 6/9/09								
67	Final Course Final Cleanup	2 days	Mon 2/23/09	Tue 2/24/09		District						
68	School Based Schedulers Entering Course Requests	28 days	Wed 2/25/09	Fri 4/3/09	67	District						
69	Onsite Training on PowerSchool Scheduling	3 days	Mon 4/6/09	Wed 4/8/09	68	District,PowerSchool						
70	Setup procedure to update students and teacher data on a regular basis to keep data current for scheduling	44 days	Thu 4/9/09	Tue 6/9/09	69	District						
71	Complete Prepare to Load Tasks (Parameters, Changes to master Schedule, Course Request etc.)	44 days	Thu 4/9/09	Tue 6/9/09	69	District						
72	Continue to work on schedule until ready to commit	44 days	Thu 4/9/09	Tue 6/9/09	69	District						
73	Commit Schedule	44 days	Thu 4/9/09	Tue 6/9/09		District						
74	<b>Preparation for 2009/10 School Year</b>	31 days	Mon 6/1/09	Mon 7/13/09								
75	Complete End of Year Process to promote students	1 day	Mon 7/6/09	Mon 7/6/09		District						
76	Check / Review Term related setup for 2009/10	2 days	Tue 7/7/09	Wed 7/8/09	75	District						
77	Import additional student information and Final Data Conversion	1 day	Wed 7/8/09	Wed 7/8/09		District,PowerSchool						
78	Copy and amend or Create Elementary School Schedules - use mass enroll to schedule students.	3 days	Thu 7/9/09	Mon 7/13/09	77	District,PowerSchool						
79	Distribute Letters to District Staff to Provide Summer Plan for Training	10 days	Mon 6/1/09	Fri 6/12/09		District						
80	<b>Summer Training</b>	30 days	Wed 7/15/09	Tue 8/25/09		District						
81	<b>Train the Trainer Training Sessions for IPT and Power Teachers for the following groups</b>	30 days	Wed 7/15/09	Tue 8/25/09	79	PowerSchool,District						
82	Attendance, Teachers, Administrators, Nurses, Clerical Staff etc.	30 days	Wed 7/15/09	Tue 8/25/09	79	District,PowerSchool						
83	<b>Train District Staff</b>	30 days	Wed 7/15/09	Tue 8/25/09		District						
84	Attendance Reports	30 days	Wed 7/15/09	Tue 8/25/09		District						
85	Report Cards and Form Letters	30 days	Wed 7/15/09	Tue 8/25/09		District						
86	PowerGrade/PowerSchool Teacher Training	30 days	Wed 7/15/09	Tue 8/25/09		District						
87	<b>Transition to Support</b>	2 days	Mon 7/27/09	Tue 7/28/09								
88	Verify Technical Contacts	1 day	Mon 7/27/09	Mon 7/27/09	51	District						
89	Transition to Technical Support	1 day	Tue 7/28/09	Tue 7/28/09	88	District,PowerSchool						
90	<b>Post-Implementation Support</b>	1 day	Wed 7/29/09	Wed 7/29/09		District,PowerSchool						

Project: PowerSchool Project Impleme  
Date: Fri 3/6/09










Task Progress Summary External Tasks Deadline


Split Milestone Project Summary External Milestone

9%







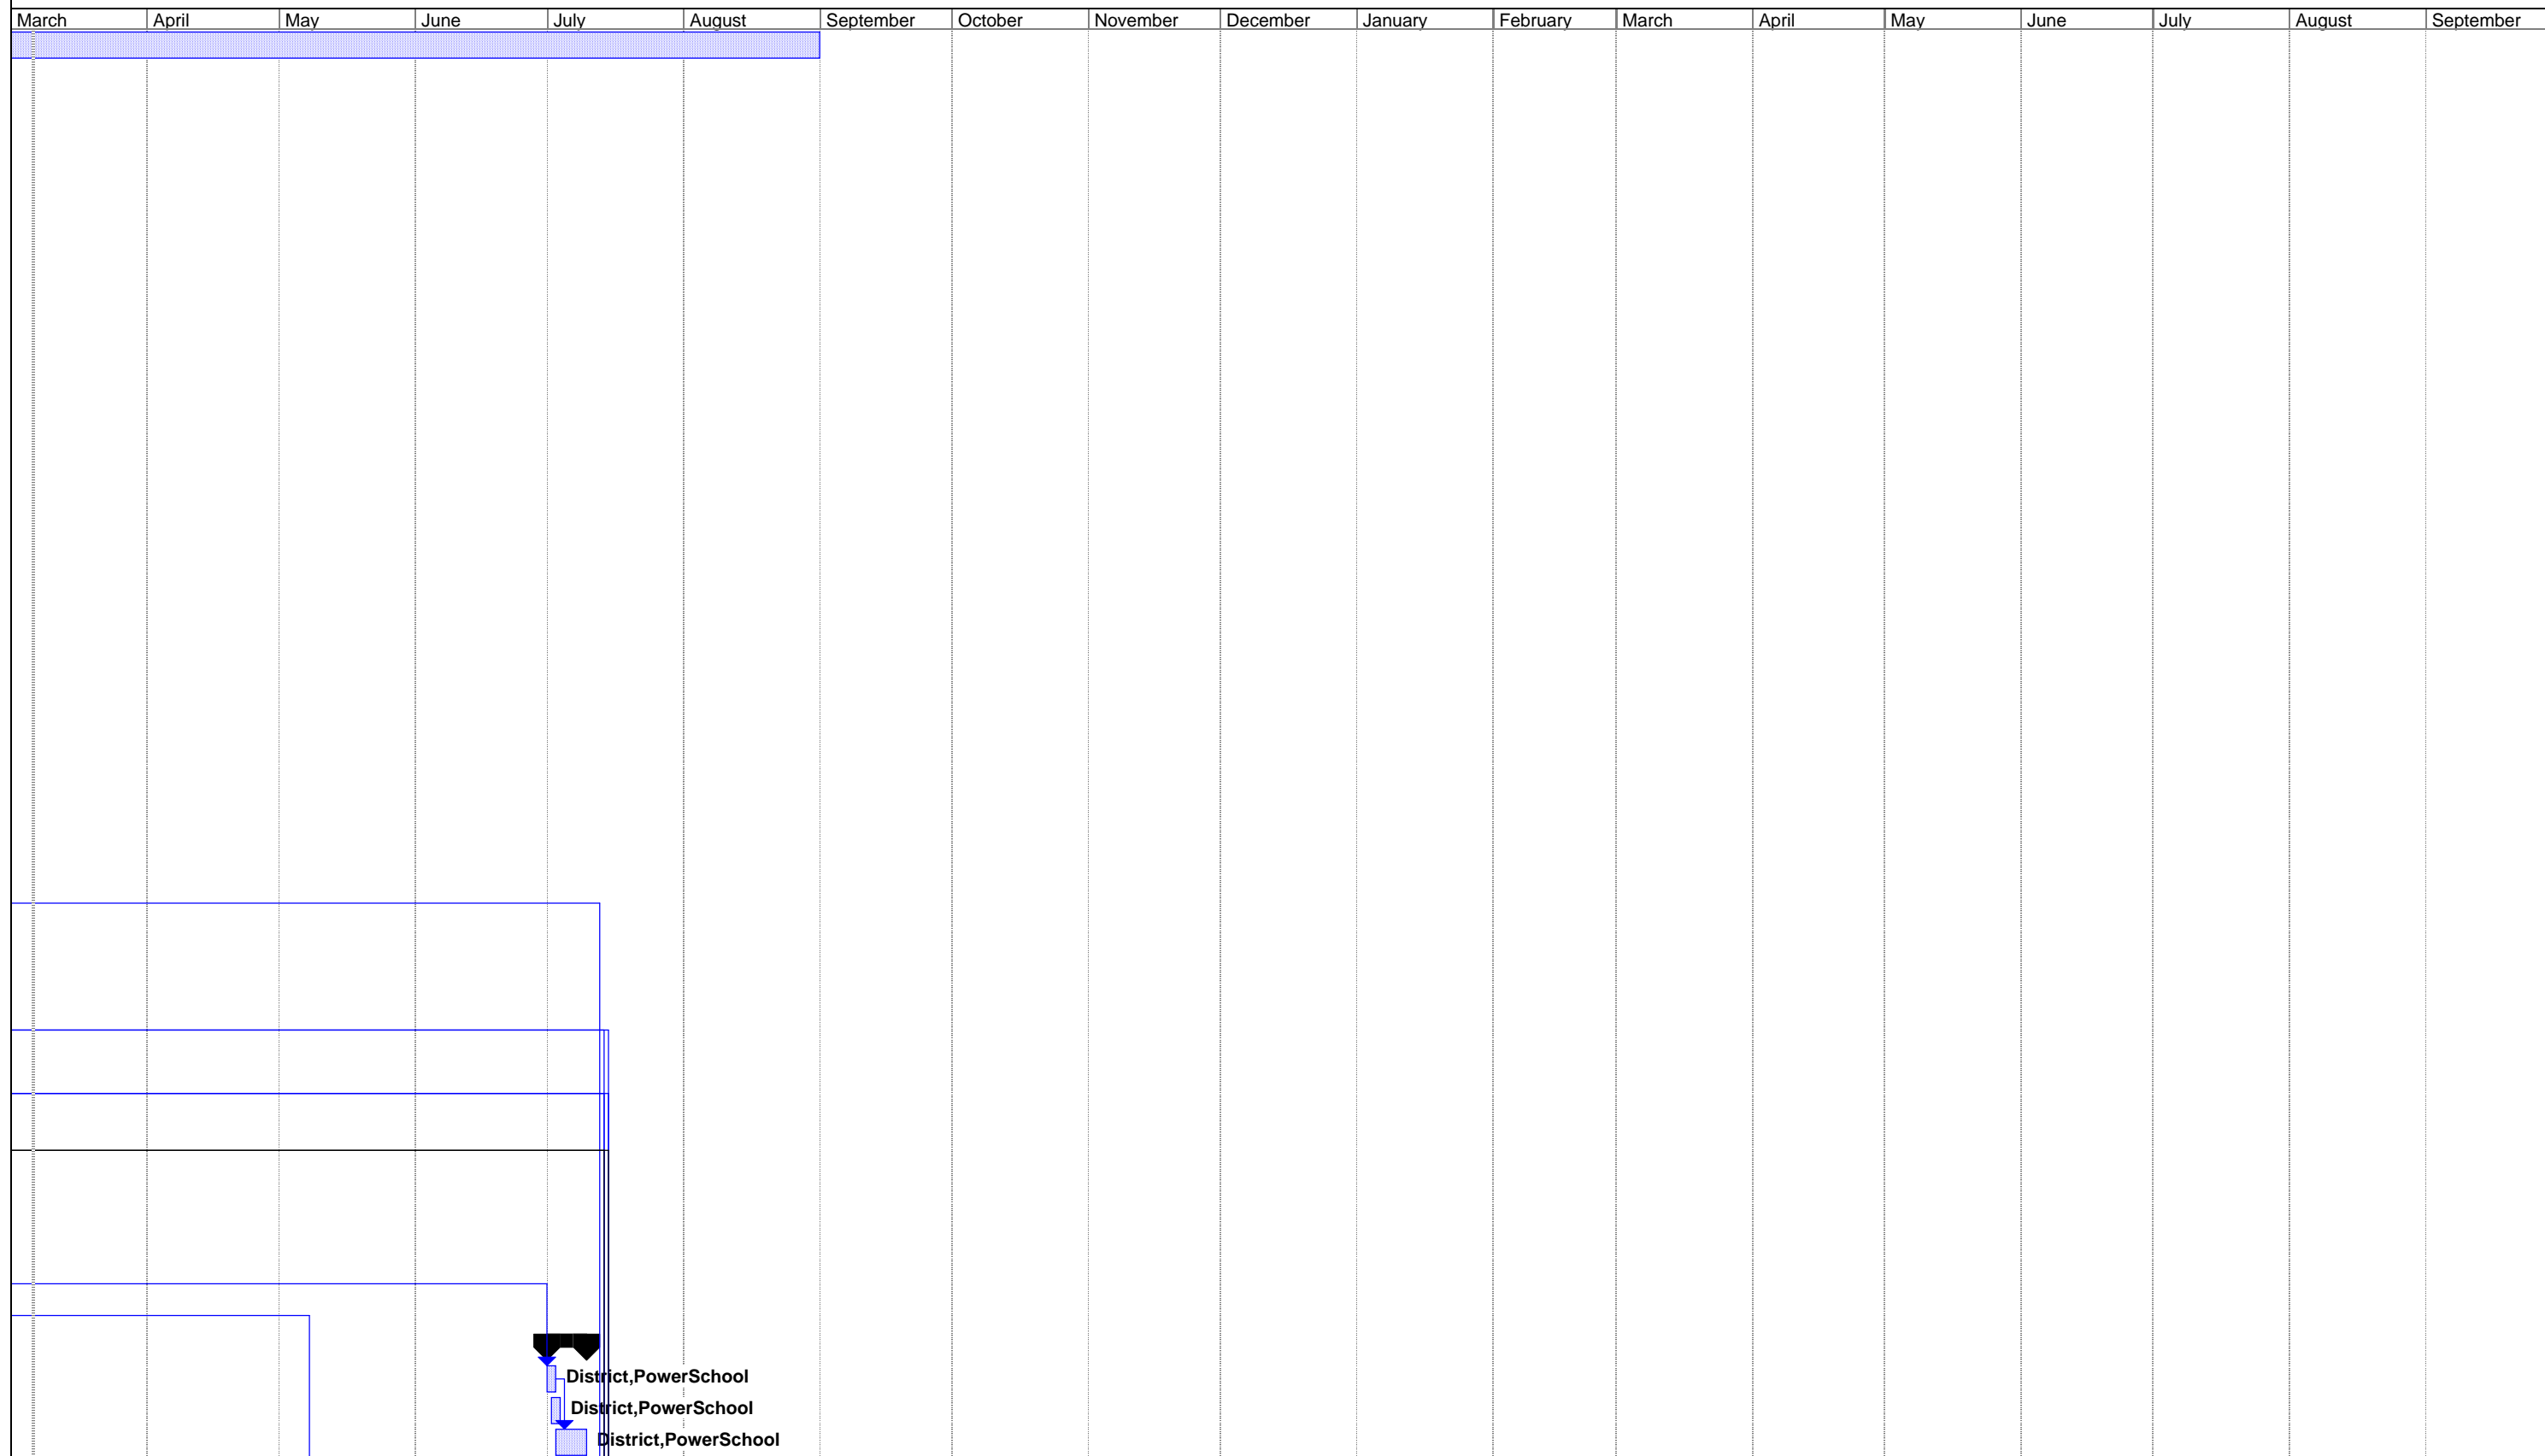


ID	Task Name	Duration	Start	Finish	Predece	Resource Names	September	October	November	December	January	February
91	<b>PowerSchool Go Live</b>	0 days	Wed 7/29/09	Wed 7/29/09	90	District						
92	<b>Roll out Parent/Student Access</b>	5 days	Mon 2/8/10	Fri 2/12/10		District						
93	<b>Advanced Training</b>	3 days	Mon 8/2/10	Wed 8/4/10								
94	Assess Advanced Training Needs	3 days	Mon 8/2/10	Wed 8/4/10		District						
95	Schedule Advanced Training	3 days	Mon 8/2/10	Wed 8/4/10		District						


Project: PowerSchool Project Impleme  
Date: Fri 3/6/09

Task  Progress  Summary  External Tasks  Deadline   
 Split  Milestone  Project Summary  External Milestone 



Project: PowerSchool Project Impleme  
Date: Fri 3/6/09

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

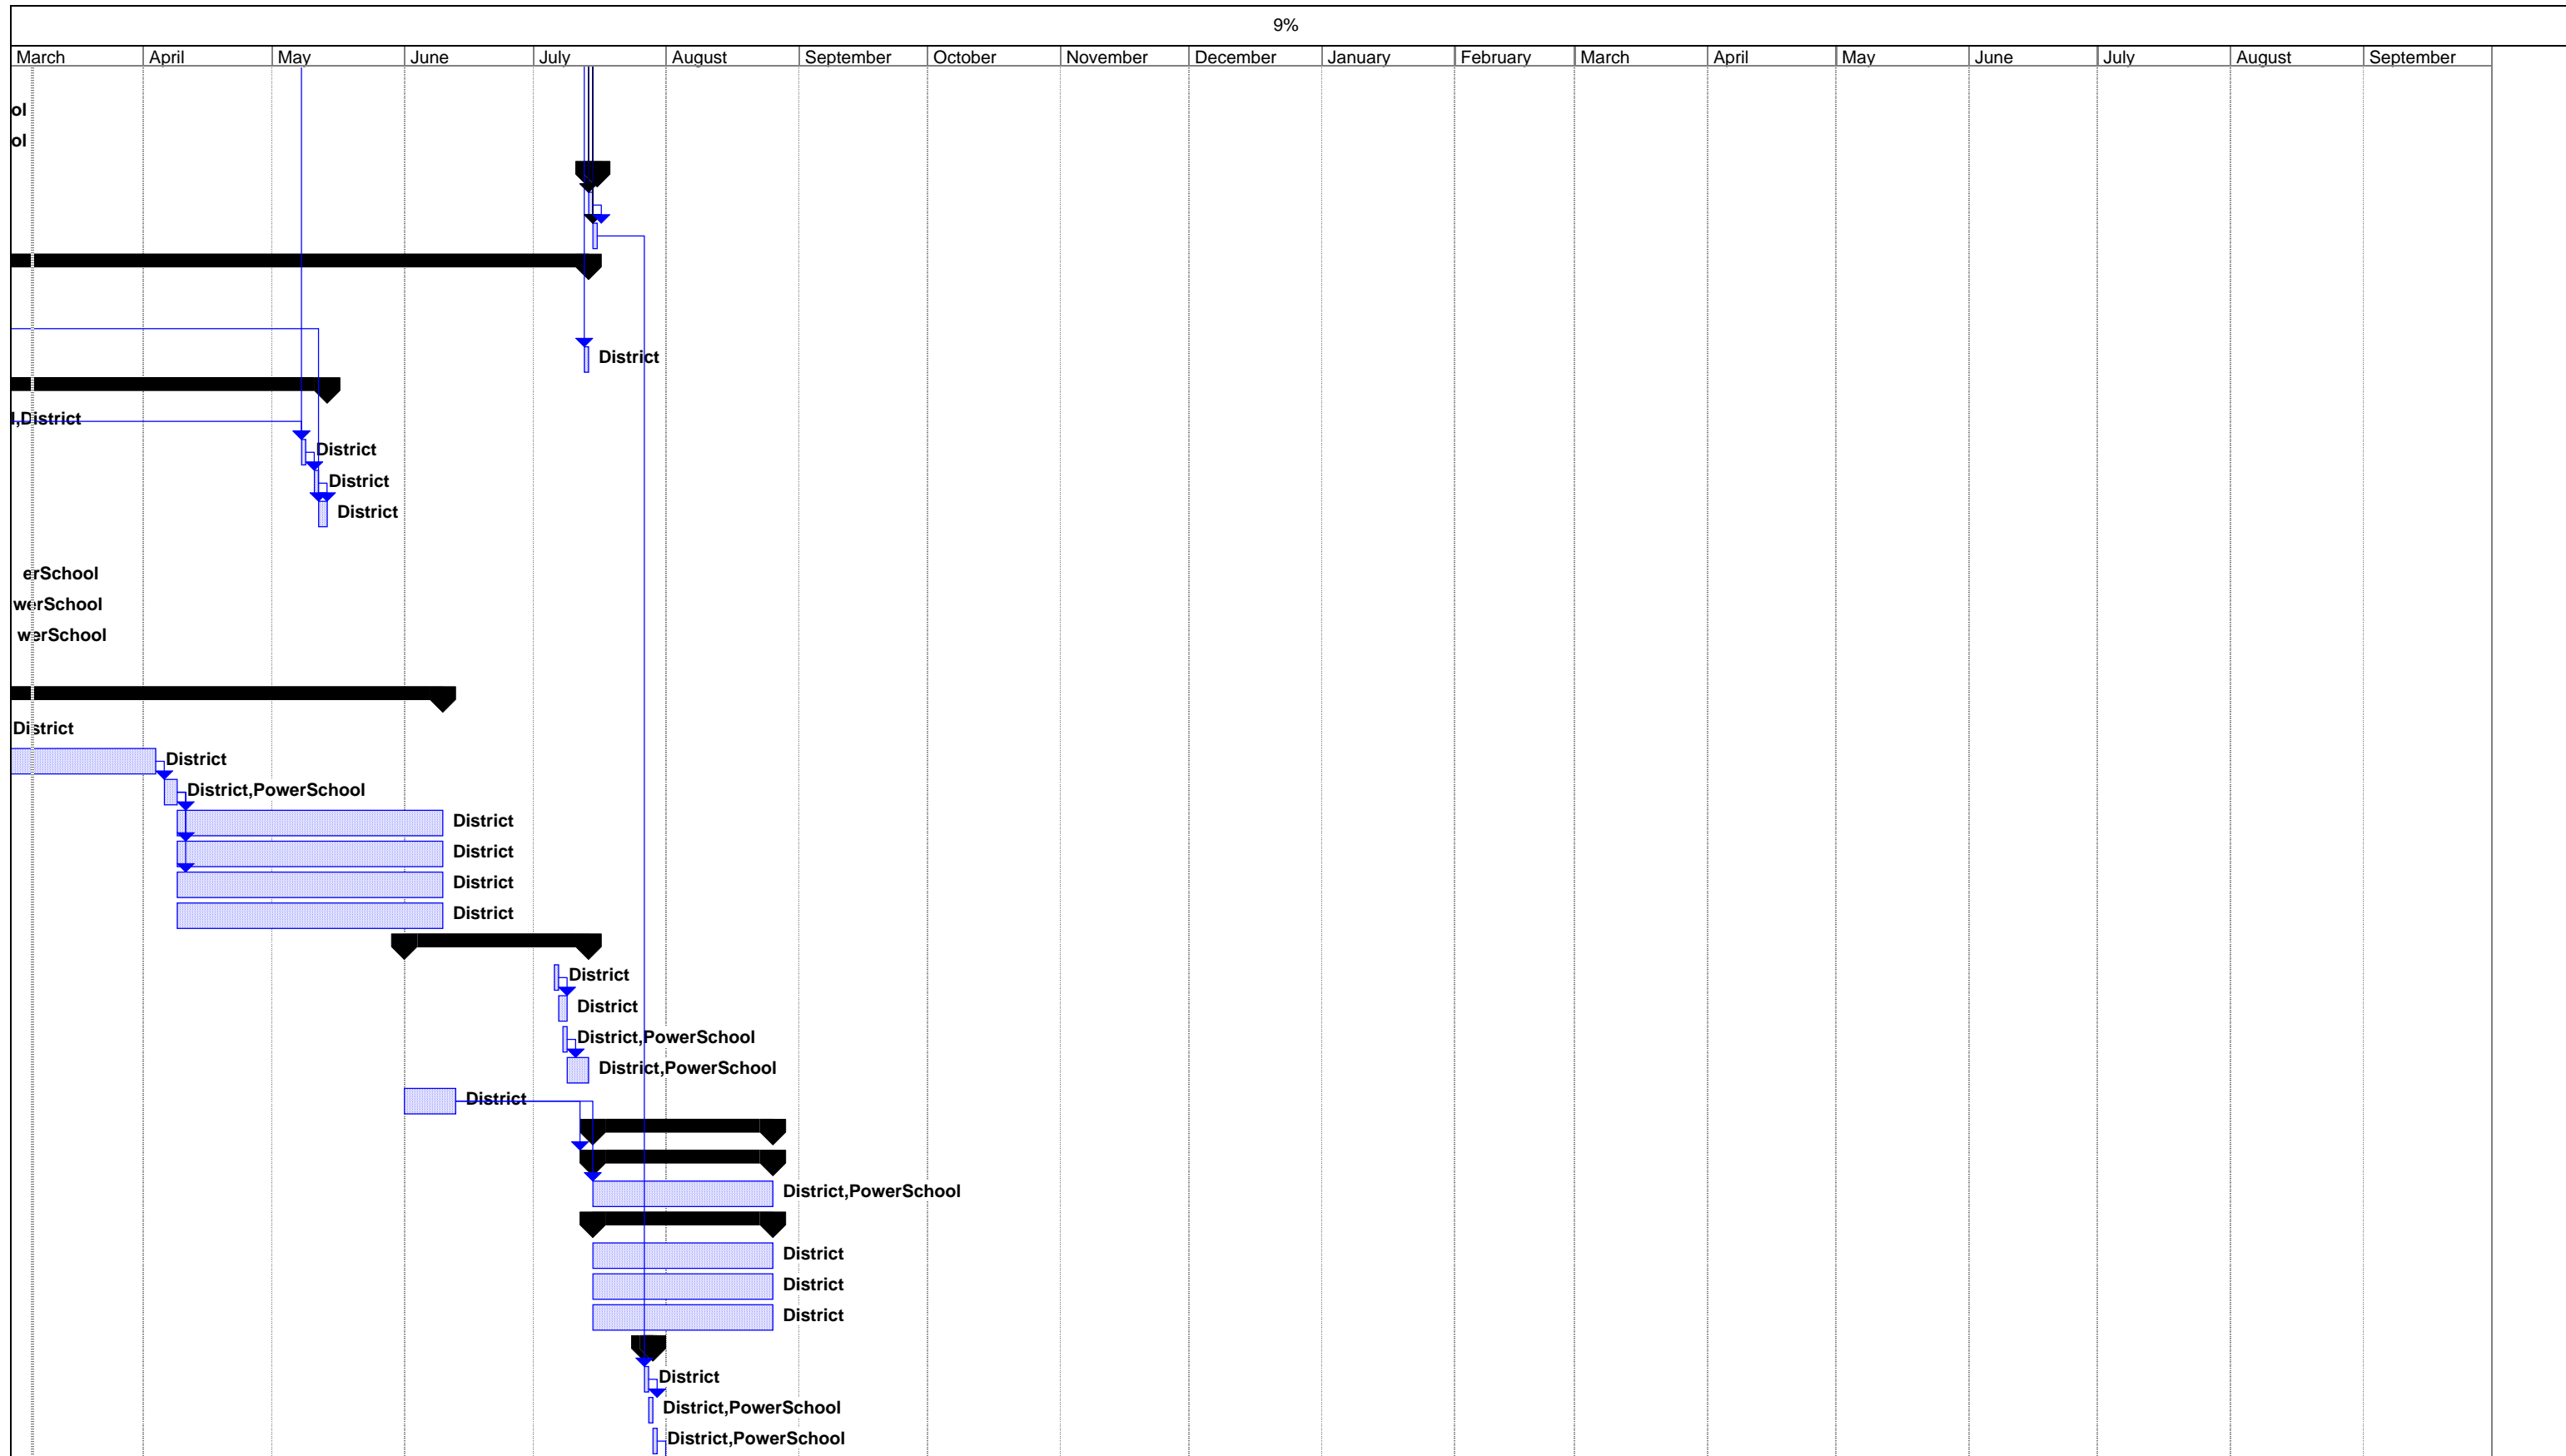









Project: PowerSchool Project Impleme  
Date: Fri 3/6/09

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September
					7/29						District						District	District

Project: PowerSchool Project Impleme  
Date: Fri 3/6/09

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone	
